



# CHANGE REQUEST

Request Nbr. 000022  
Request Date 18-Apr-2022  
Customer ID 0806  
Currency USD  
Project Nbr. 21-940  
Contract Time Change, Days  
Description PR #15 Cover Electric Panel

Breiholz Construction  
1527 Maine St  
Des Moines, IA, 50314  
Phone: 515-288-6077  
Web: www.breiholz.com

## ESTIMATION

NO. PROJECT TASK	DESCRIPTION	QTY UOM	LINE AMT
1	Drywall labor and Materials	1.00 LS	941.27

Approved Amount of Change (USD): 941.27

## CONTRACTOR

Breiholz Construction  
1527 Maine St  
Des Moines, IA, 50314  
Phone: 515-288-6077  
Web: www.breiholz.com

18-Apr-2022

*Scott Rozenboom*

(signature)

## OWNER

Marshall County  
1 E Main St  
Marshalltown, IA, 50158

18-Apr-2022

(signature)

# PROPOSAL REQUEST

**PR NO.: 015**


<b>PROJECT NAME:</b>	Marshall County Courthouse	<b>PROJECT NO:</b>	18827003
<b>CLIENT NAME:</b>	Marshall County	<b>DATE:</b>	15 March 2022
<b>PROJECT LOCATION:</b>	1 E Main St Marshalltown, IA 50158	<b>CONTACT:</b>	Jimi Peters
<b>GENERAL CONTRACTOR:</b>	Breiholz Construction		

The following Proposal Request is issued to request an estimate for Owner's further consideration. No work is to occur until approval is received in writing. Proceeding with the Work prior to authorization indicates your acknowledgement that there will be no change in the Contract Sum or Contract Time.

**Description:**

Please consider the following replacement scope of work for the existing electrical panel in workroom 124:

02 26 02 EXISTING ELECTRICAL paneled wall to remain, modify panels and paint to match adjacent wall (SEE ELECTRICAL)

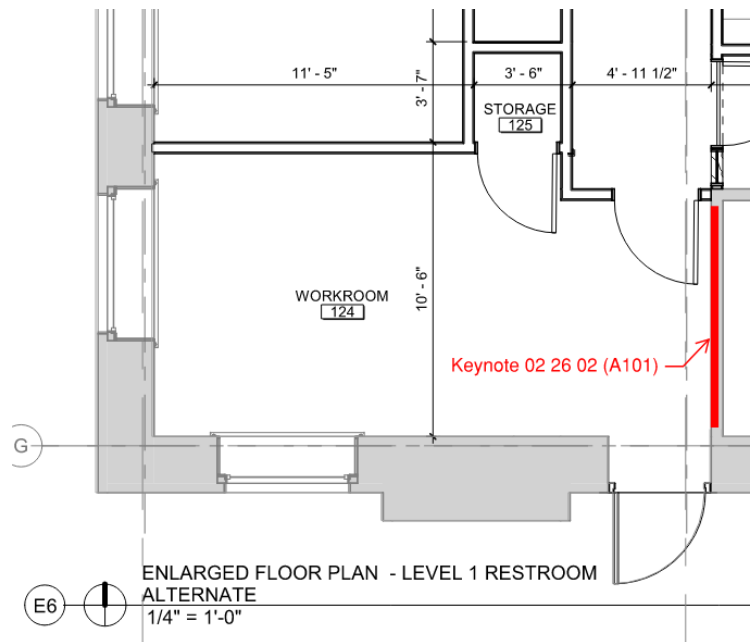

1. **REPLACE** modification & painting of existing metal panels with the following scope of work.
  - a. Have Electrical Contractor Ensure the Panels are not connected to power.
  - b. Remove Panel doors/covers back to steel frame
  - c. Install plywood, and 5/8" gypsum wall board to flush out with surrounding gypsum board. Verify plywood thickness on site, shimming may be required to flush out the gypsum board wall surfaces.

**Attachments:**

n/a

Jimi Peters, AIA  
 OPN Architects, Inc.  
 cc: Scott C. Allen, AIA
